

2019 Bond Program Update




Septic System

- After a lengthy design and review process, the septic design was approved in early summer allowing replacement of the MS/HS systems to begin in August.
- Installation and startup of the new system took place in early September and the MS/HS has now been disconnected from the old system making way for the new Art/Music/Weight Room addition to move forward!



MS/HS Building Renovations & Additions

- Renovations to the existing bathrooms took place this summer and were completed on schedule.
- Site work has commenced for the new bus garage, Art/Music/Weight Room addition, Ag barn and greenhouse.
- The new Ag barn is under construction scheduled for completion this fall.
- The new bus garage is scheduled to be completed at the end of the year.
- The Art/Music/Weight Room addition is scheduled for completion in the summer of 2022.

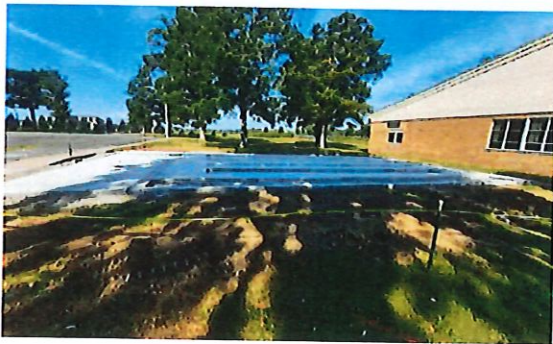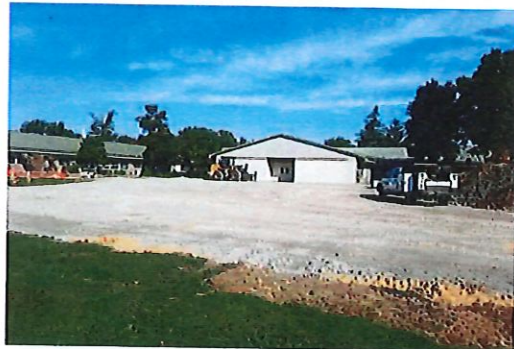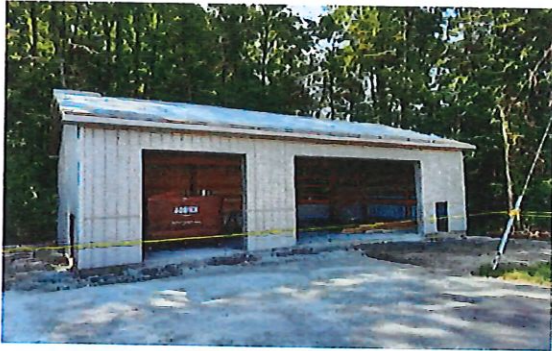

For more information, visit
www.whiteford.k12.mi.us/bond
